

# EXECUTIVE SUMMARY REPORT

PROVIDED BY FINDORFF



MIDDLETON-CROSS PLAINS AREA SCHOOL DISTRICT  
BUILDING FOR OUR FUTURE

POPE FARM ELEMENTARY SCHOOL | 07.02.2020

## What's New?

On-site, curb and gutter has been added to complete the school lot. Concrete sidewalk is poured in front of the east entryway and continues around the drop-off loop. East and west entryways are nearing completion and the west canopy is complete with metal panels.

Inside, the new finishes are bringing the building to life. Graphic murals have been installed above the social stairs and behind the LMC reception desk. Decorative decals, signs, and room signage have been added around the building. The ceiling subcontractor has also placed cloud ceilings in the common areas for each grade. The flooring subcontractor nears completion on the first floor classroom areas, as well as the office area. The carpenters have completed all locker cubby areas and are working on finishing the display cases with the finish woodwork and hanging doors. Student furniture has also begun being added to classrooms.



## DRONE FOOTAGE

Click on the image to check out the latest progress!

## The Past Week:

- Began Adding Graphics to Interior Walls
- Carpeting Started in the Administration Area
- Final Finishing on the Gym Floor
- Completed Metal Panels on West Canopy

## Coming Up in the Week Ahead:

- Carpeting in the LMC
- Finishing Display Cases
- Completing Atrium Baffles



Sunflower graphic added behind the LMC reception desk.



## DID YOU KNOW?

Graphic murals, such as the one behind the social stairs, can be designed to fit a large wall, but it must be broken into smaller pieces for application. The middle section was hung from the balcony, and the graphic was brushed onto the wall starting in the middle and working out to prevent air bubbles. The adjacent sections were placed next, making sure that the ends matched to create a seamless look.

QUESTIONS?

Please contact Project Manager Tanner Davis at [tdavis@findorff.com](mailto:tdavis@findorff.com)

**Findorff**



Graphic added above the social stairs in the atrium area.



Kindergarten and bumblebee signs added next to the display case.




Vinyl flooring added in parts of the administrative area.

# EXECUTIVE SUMMARY REPORT



*Cloud ceiling and hexagon lights added to the Kindergarten common area.*

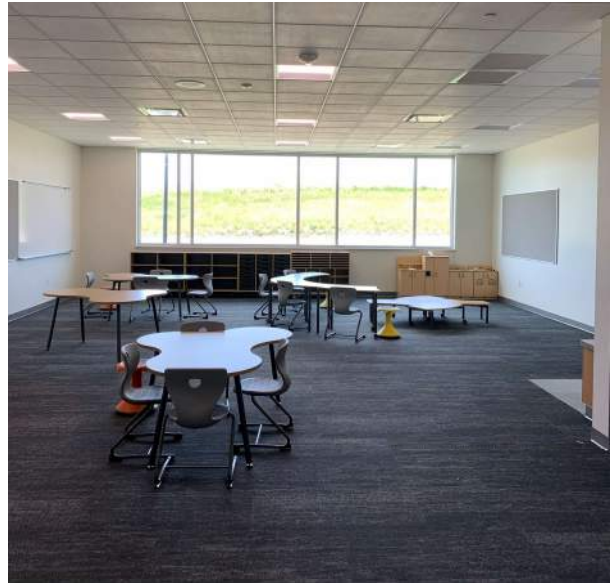

*Furniture set in a Kindergarten classroom.*



*Curb, gutter, and sidewalk poured around the parent drop-off loop.*



*Entryway doors and frames installed on the west side of the building and the metal paneling has been completed on the canopy.*

**QUESTIONS?**

Please contact Project Manager Tanner Davis at [tdavis@findorff.com](mailto:tdavis@findorff.com)

**Findorff**
