

EXECUTIVE SUMMARY REPORT

PROVIDED BY FINDORFF



MIDDLETON-CROSS PLAINS AREA SCHOOL DISTRICT
BUILDING FOR OUR FUTURE

PARK ELEMENTARY SCHOOL | 08.28.2020

What's New?

The building is nearing completion and the carpenters are making final adjustments. Inside, rain drop coat hooks have been added to the wall in the cafeteria. Hanging clouds have also been installed in the cafeteria and the vestibule. Epoxy flooring has been added to the new receiving room. Wall cabinets have been hung in the new classroom. Other interior punchlist items are being addressed.

Outside, graded areas were seeded and watered and grass is growing. Basketball hoops have arrived and are waiting to be installed. The large grass field to the west of the school has been seeded. The retention pond next to the new parking lot has been seeded.



DRONE FOOTAGE


Click on the image to check out the latest progress!

The Past Week:

- Rain Drop Coat Hooks Hung in Cafeteria
- Epoxy Flooring Set in the Receiving Room
- Wall Cabinets Hung in the New Classroom
- Seeding and Watering around the Addition

Coming Up in the Week Ahead:

- Pouring the Garage Flooring
- Hanging the Shades in the Cafeteria
- Installing the Basketball Hoops
- Finishing up Final Punchlist Items

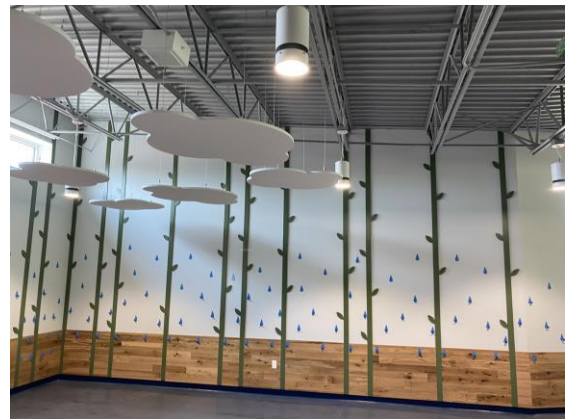

Rain drop coat hooks added to the wall in the cafeteria.



DID YOU KNOW?

The punchlist is an important step in the Findorff close-out process. This is where we meet with the owner and the architect and review the building. We usually take notice of paint chips, flooring issues, missing items, etc. During the punchlist we gather up a list of items needed to be fixed and distribute them accordingly to the subs. This allows an organized way of making sure these items get noticed.

QUESTIONS?

Please contact Project Manager Jacob Jankowski at jjankowski@findorff.com

Findorff

EXECUTIVE SUMMARY REPORT



PARK ELEMENTARY SCHOOL | 08.28.2020

Page 2



Seeding has been completed around the addition.



Wall-hanging cabinets hung in the new classroom.



Epoxy flooring completed in the new receiving room.



Hanging cloud decorations in the cafeteria vestibule.

QUESTIONS?

Please contact Project Manager Jacob Jankowski at jjankowski@findorff.com

Findorff
